BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Anam Enclave in ward No. 06 Thanisandra Village Limits	
2	Estimate Cost	30.00 Lakhs	
3	Administrative Approved No and Date	521/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	372/13-14, Date. 03.03.2014	
5	Job Code No. and P Code No.	006-14-000056	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	412/2013-14, Date.21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	01.06.2014	
12	Actiual Date of Completion	25.06.2014	
13	Delay if any	Nil	

14	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	16.07.2015	
19	MB No. and Page No.	Mb 8909 Page No.190859-870	
20	BR No. and Date	181/30.06.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultant and Engineers is verified and Enclosed	
22	Section officer	Sri K Devegowda J.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

16/07/15

Y C Kale gowda
Executive Engineer (Retd)

Executive Engineer
Byatarayanapura Division
Yalahanka Zone, B.B.M.P.
Bangalore-560092

Anam Enclve

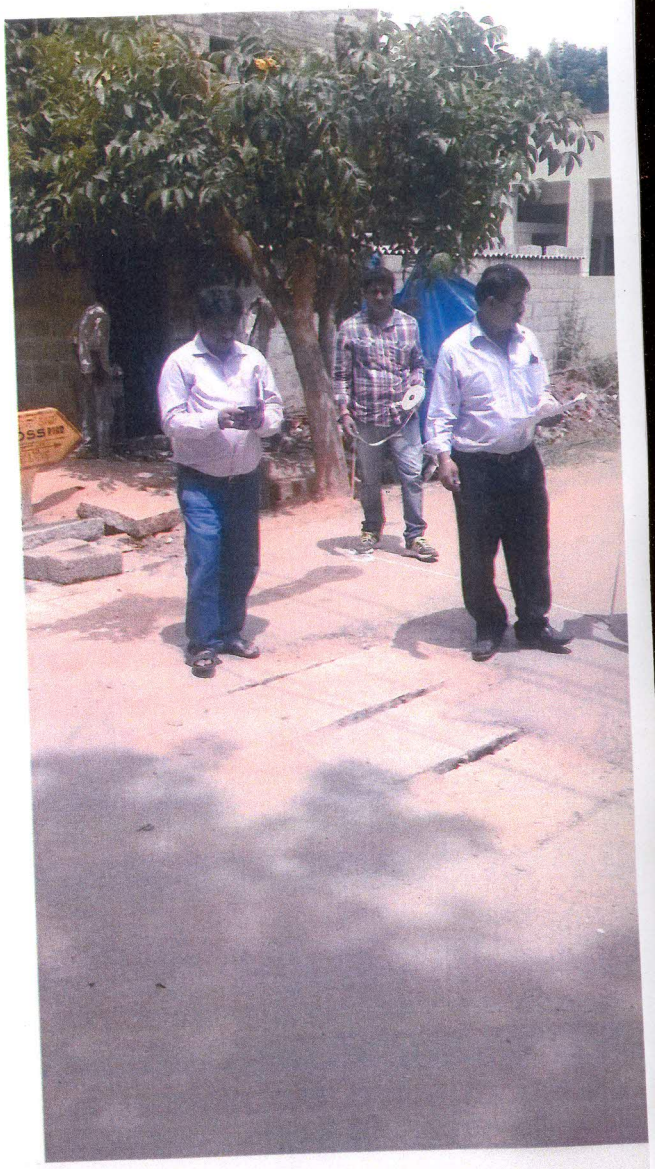

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

Improvements to Roads and Drains at Anam Enclave in Ward No. 06 in Thanisandra Village Limits.
